Annex I

Project Status Report on Cajamarca Water Supply and Sewerage Improvement and Expansion Project Loan Agreement No PE-P35 First Quarter Report

Organization Information

	Dirección Genera	l de Endeudamiento y Tesoro Público	
		nomía y Finanzas	
		Carlos Linares Peñaloza	
Borrower		Director General	
	Contacts	Address: Jr. Junín № 319 Lima 1 - Perú	
		Phone/FAX: 51-1-3115931 / 51-1-6269921	
		Email:	
	Unidad Ejecutora	de Programas Regionales - PROREGION	
	Regional Govern	ment of Cajamarca	
	Person in Charge	José Panta Quiroga	
Executing Agency		Director Ejecutivo	
Executing Agency	Contacts	Address: Jr. Sta. Teresa de Journet 351,	
		Urb. Horacio Zevallos - Mz. G-5, Cajamarca, Perú	
		Phone/FAX: 51-076-344364	
		Email: jp_consultor@hotmail.com	
	EPS SEDACAJ		
	Person in Charge	Luis Llanos Ramírez	
		Gerente General	
	Contacts	Address: Jr.Cruz de Piedra No 150-Cajamarca-Perú	
	1	Phone/FAX: 51-076-362121 / 51-076-362167	
Implementing]	Email: <u>sedacaj@terra.com.pe</u>	
Agencies	EPS Marañon		
	Person in Charge	Marino Soto Herrera	
		Gerente General	
	Contacts	Address: Jr.Mariscal Ureta Nol912 - Jaen - Perú	
		Phone/Fax:51-431-618	
		Email: <u>epsmaranon@speedy.com.pe</u>	
	Vice Ministerio de Construcción y Saneamiento		
	Ministerio de Viv	rienda, Construcción y Saneamiento	
Monitoring Agency	Person in Charge	Felix Agapito Acosta	
Monitoring Agency		Vice Ministro	
	Contacts	Addre ss: Av. Paseo de la República 3361 - San	
		Isidro - Lima - Perú	
		Phone/ FAX: 51-1-2117930 Ax. 1801 / 51-1-2117945	
		Email: afelix@vivienda.gob.pe	

Outline of Loan Agreement:

Source of Finance	JICA: Not exceeding ¥ <u>4,995 mil.</u> Government of <u>the Republic of Peru:</u> ¥6,138 mil.
Terms and Conditions	For JICA -Interest Rate:

1: Project Description (Relevance)

1-1 Project Objective

Original: (P/M)

To improve sanitary conditions of Region of Cajamarca by rehabilitating and expanding the water supply and sewerage facilities in 11 provincial cities, thereby providing safe and reliable services.

Modified objective and its reason(s):(P/R ami PCR.)

1-2 Necessity and Priority of the Project

Consistency with development policy, sector plan, national/regional development plans and demand of target group and the recipient country.

Original: (P/M)

(1) Sanitation Sector in Peru

1. The Millennium Development Goals (MDGs) states one of its goals as "Ensure Environmental Sustainability" (Goal 7) and sets "Reduce by half the proportion of people without sustainable access to safe drinking water and sanitation" (Target 10) as one of the targets to be archived. In Peru, in order to achieve such target, National Plan on Sanitation 2006-2015 of Peru advocates modernization of management system, improvement of sustainability and quality of services provided and financial conditions of service provider, and expansion of existing potable water and sewerage system. Its specific goals include:

Table 1: Main goals stated in National Plan on Sanitation 2006-2015 (Sanitation Indicators)

	2005	2010	2015
Connection Rate (Potable Water)	76%	79%	82%
Connection Rate (Sewage)	57%	66%	77%
Sewage Treatment Rate	22%	54%	100%
Service Hours a Day	17h	22h	23h
Micrometer Coverage	54%	92%	95%

2. In order to achieve these goals, the Government of Peru (GOP) represented by Ministerio de Vivienda, Construcción y Saneamiento (MVCS) estimates that until 2015 it needs USD 4,042 million for investment to the sector, and establishes the following basic financing policy;

Area	Service responsibility Resources lor investment		investment
		Water supply	Sewerage
Large urban area	Large and Medium EPS	EPS's own resourceLoan repaid by EPSPrivate participation	EPS's own resourceLoan repaid by EPSPrivate participation
Medium urban area	Small EPS and Municipalities	- Own resource	- Own resource
Small urban area and rural area	Municipalities and communities	- GOP budget	- GOP budget

- 3. The GOP aims that the investments by the GOP budget should be minimum, concentrating mainly to the small urban area and rural area where financial autonomy of the municipalities and communities is very hard to achieve, and that in large urban area the EPS should be responsible for investments. However, it is becoming clear that in some cases the service responsible entities are not capable to finance their investment needs, especially for (i) large scale of sewerage projects because the large scale investment for sewerage facilities (especially treatment) is sometimes not rentable even for large EPS, and (ii) projects in medium urban area, because the investment scale is often too large for small EPS and the municipalities, due to their limited financial capacities by their smaller size of activities.
- 4. The GOP has started in 2006 the Program "Agua para Todos" to support investments of EPS and the municipalities with GOP budget. However, since the needs for investment exceed the resources allocated to the PAPT, the GOP now is studying the introduction of alternative financial scheme by combing the external loan with the participation of the Regional Governments.

(2) Sanitation Sector in Region of Cajamarca

1. The Region of Cajamarca, which consists of 13 provinces and 127districts, is located in the northern part of Sierra(highland) of Peru. It is the 4th poorest region among 25 regions in Peru, whose living conditions are much lower than the national average¹;

Region of Cajamarca		Peru
poverty line and those who live	74.2% below poverty line 36.9% blow extreme poverty	51.6% below poverty 19.2% below extreme poverty
below extreme poverty		
Average Income (year)	S/. 468.81 (Per month)	

2. The major part of water supply and sewerage facilities in provincial cities of Cajamarca were constructed during 1960s and 1970s by national government. Due to principally long period of usage and sometimes lack of adequate and timely investments and O&M (operation and maintenance), these water supply and sewerage systems have serious problems such as (i) deteriorate water quality, (ii) limited water service hour, (iii) contamination through untreated waste water, among others.

¹ Peru Opportunities for All, Peru Poverty Assessment, World Bank, December 2005,p.l8 and 173.

							(Unit:%)
	Cajamarca	Peru			Latin America		l .
	Urban	Total	Urban	Rural	Total	Urban	Rural
Water coverage rate	72.2	83	89	65	91	96	73
Sewerage coverage rate	73.6	63	74	32	77	86	49
Waste water treatment rate	15*'	24*2	N.A	N.A	N.A	N.A	N.A

Source : Joint Monitoring Programme, WHO&UNICEF

http://www.sunass.gob.pc/doc/indicadores/2005/evolucion indicadores 9705.pdf

City (Population)	Water Service hour	Years since installation	water coverage	Micro meter (%)	Unaccounted for Water (%)	Sewerage Coverage	Waste Water Treatment
Cajabamba (14,528)	16	50 years	59.4%	24.28%	50.1%	84.7%	0%
Celendin (16,721)	14 (dry season) 24 (rainy season)	40 years	75.1%	87.4%	41%	75.1%	0%
Conrumazá (3,221)	24	40 years	87.1%	90.5%	36.3%	83.8%	0%
San Pablo (2,940)	4 (dry season) 14 (rain)' season)	30 years	79.6%	0%	45%	75.8%	0%
San Miguel (3,635)	20 (rainy season) 12 (dry season)	40 years	81.5%	92.7%	36.6%	71.1%	0%
San Marcos (7,619)	22 (rainy season) 6 (dry season)	40 years	77.7%	94.0%	32.9%	58.6%	0%
Bamba marca (17,763)	24 (lower city) 1 (upper part)	40 years	45.6%	74.34%	35.6%	46.4%	0%
Chota (18,454)	3 (rainy season) V2 (dry season)	30 years	67.7%	0	51.8%	56.1%	0%
Cutervo (15,341)	9	40 years	65.1%	0	70.2%	74.7%	0%
Hualgayoc (1,433) '	16 (rainy season) 6 (dry season)	40 years	87.6%	0	62.96%	86.5%	0%
Jaen " ⁴ (78,097)	14	35 years	73.7%'^	23%	52.5%	63.4%	100%*'

^{*3} There is one waste water treatment plant in Jaen, however, it doesn't have enough capacity to treat inflow of sewer.

^{*1} Only two cities (Cajamarca and Jaen) have WTPs to treat sewage.

^{*2} índice Tratamiento Aguas Servidas

^{*4} The total of the population of Jaén (64,766), Fila Alta (6,799) and Bellavista 6,532) j

^{*5} For the population of Jaén only(Fila Alta and Bella vista are not included) since the pipeline and connection for Jaén is included in the scope of the Project. Bella Vista is considered only for the calculation of demand of the production of potable water.

^{*6} For the population of Jaén and Fila Alta only, since Jaén and Fila Alta are located in the same district and integrated into the same sewerage system whereas the construction of pipes and connection for Fila Alta is not included in the scope of the Project.

3. Before such situation, the Regional Government of Cajamarca (RGC) has proposed to the GOP an alternative financial scheme to the rehabilitation and expansion projects of water and sewerage systems in urban area of the Region, putting its CANON distribution revenue as the resource for repayment and counterpart fund for the external loan.

Attachment(s):		

Attachment(s): required only when they are revised.

1-3 Rationale of the Project Design

- Timing, scale, technology of the project

Original: (P/M)

(1) Timing

Water supply and sewerage systems in these provincial cities, sometimes constructed over forty years ago, are coming to end of their life.

(2) Scale

The Project is designed taking into account (i) current situation of deterioration of water supply and sewerage system and (ii) projected demand of the area up to 20 years.

(3) Technology

Technology of WTPs and WWTPs are selected based on the facility and continuity in , as follow,

Cities	WTP	WWTP		
Cajabamba	Mixed Rapid	Imhoff tank +Thricking Filter+ Secondary Sedimentation		
C 1 1:				
Celendin		Rafa (existing)+ Secondary Lagoon		
Contumaza		Anaerobic Lagoon + Facultative Lagoon (Non-JICA)		
San Pablo		Anaerobic Lagoon + Facultative Lagoon (Non- JICA) Septic Tank		
San Miguel		Anaerobic Lagoon + Facultative Lagoon (Non-JICA)		
San Marcos	Slow Filter	Lagoon (Non- JICA)		
Bambamarca		Anaerobic Lagoon+ Thricking Filter +Secondary Sedimentation Septic Tank		
Chota		Anaerobic Lagoon+ Thricking Filter +Secondary Sedimentation		
Cutervo		Anaerobic Lagoon + Facultative Lagoon		
Hualgayoc		Imhoff Tank +Soil Treatment		
Jaen	Rapid Filter	Anaerobic Lagoon+ Facultative Lagoon		

Actual: (P/R, PCR)

2: Project Implementation (Efficiency)

2-1 Project Scope

Table 2-1-la: Comparison of Original and Actual Location

	Original: (P/M)	
	Water Supply and Sewerage	
	(11 provincial cities)	
	Bambamarca, Cajabamba, Celendin,	Actual: (P/RandPCR)
Location	Chota, Contumaza, Cutervo,	
	Hualgayoc, Jaen, San Marcos, San	Attachment(s):Map
	Miguel, San Pablo	
	Attachment(s):Map	

Table 2-1-lb: Comparison of Original and Actual Scope

Items	Original	Actual
Water Supply		
Intake	- 9 cities -14 intake points (1 construction: 11.00 1/s, 13 rehabilitation: 211.04 1/s)	- 9 cities -14 intake points (1 construction: 11.00 1/s, 13 rehabilitation: 211.04 1/s)
Treatment Plant	- 4 cities - 4 plants (3 construction: 229.6 1/s, 1 rehabilitation: 10 m³)	- 4 cities - 4 plants (3 construction: 229.6 1/s, 1 rehabilitation: 10 m³)
Conduction	-10 cities (2 construction: 19.1 km, 10 rehabilitation: 57 km)	-10 cities (1 construction: 14.114 km, 10 rehabilitation: 68.817 km)
Reservoir	- 8 cities -18 reservoirs (07 construction: 7,440 m) (11 rehabilitation: 3,934m³)	- 8 cities -18 reservoirs (07 construction: 7,440 m) (11 rehabilitation: 3,934m³)
Pipe Line (Primary and Secondary Line)	- 65.416 km (construction) -191.020 km (rehabilitation)	- 89.521 km (construction) -201.715 km (rehabilitation)
Connection	 30,365 21,033 (rehabilitation) 9,332 (construction) 	31,35023,327 (rehabilitation)8,023 (construction)
Sewerage		
Connection	 30,551 18,383 (rehabilitation) 12,168 (construction) 	 28,399 15,900 (rehabilitation) 12,499 (construction)

Items	Original	PSR prepared on June 27, 2012 Actual
Secondary Line	-11 cities	- 11 cities
	- 257.726 km	- 281.915 km
	- 188.396 km .(rehabilitation)	- 180.358 km .(rehabilitation)
	, , ,	,
Pumping Station	- 69.330 km. (construction)	- 101.557 km. (construction)
Tumping Station	- 2 cities	- 2 cities
	- 3 pumps	- 3 pumps
Datasas Itas	(3 construction: 360.28 m / day)	(3 construction: 360.28 m / day)
Primary Line	- 08 cities	- 08 cities
	- 15.215 km	- 10.355 km
	- 3.457km (rehabilitation)	- 3.207 km (rehabilitation)
	- 11.758 km (construction)	- 7.148 km (construction)
Treatment Plant	- 8 cities	- 8 cities
	-12 plants (6 lagoons, 2 Imhoff,	4 -12 plants (6 lagoons, 2 Imhoff, 4
	septics tanks), 4 plants constructe	d septics tanks), 4 plants constructed
	by counterpart fund) (11 construction	n: by counterpart fund) (11 construction:
	18,517 rrf/day) (01 rehabilitation	n: 18,517 rrf/day) (01 rehabilitation:
	293.8 m ³ /day)	293.8 m ³ /day)
Consulting Services	1) Preparation of EI A	1) Preparation of EI A
	2) Detailed Design	2) Detailed Design
	3) Assistance for Preparation of	of 3) Assistance for Preparation of
	Bidding Documents	Bidding Documents
	4) Tendering Assistance	4) Tendering Assistance
	5) Supervision of Civil Works	5) Supervision of Civil Works
	6) Technical Assistance and	d 6) Technical Assistance and
	Start-ups	Start-ups
	7) Technical Assistance	7) Technical Assistance
	(Awareness raising: hygien	ne (Awareness raising: hygiene
	education, promotion of hous	se education, promotion of house
	connection, Institution	al connection, Institutional
	Capacity building, Advisory services	Capacity building, Advisory services)

2-1-2 Reason(s) for the modification if there have been any.

(P/R and PCR)

2-2 Implementation Schedule

Table 2-2-1: Comparison of Original and Actual Schedule

Items	Original	Actual
[P/M]	(P/M)	(P/R,PCR)
* it will be modified according to the		
final version of the Implementation		
Schedule of the mission of this time.		
Signing of Loan Agreement	March, 2009	March, 2009
Preparation of Short List, TOR and	December, 2008 - February, 2009	
Invitation Letter and JICA Concurrence		
Invitation and Evaluation of	March- May, 2009	March 12, 2009
Proposal and JICA Concurrence		
	June July 2000	April 28, 2009
Negotiation and Signing of Contract and	Julie - July, 2009	April 28, 2009
JICA Concurrence	A 2000 I 2010	
Detailed Design Preparation of Tender Documents	August, 2009 - January, 2010	
-		D 1 00 0000
for Civil Works and JICA	November, 2009 -July, 2010	December 29, 2009
Concurrence		
Tender Period	February - April, 2010	June 30, 2010
Tender Evaluation and JICA Concurrence	April, 2010	
Negotiation and Signing of Contract and	May - July, 2010	Group A – July 27, 2010
JICA Concurrence		Group B - July 27, 2010
		Group C - July 27, 2010
Project Completion Date*	November 2011	Group A -January 2012
		Group B - May 2012
		Group C - April 2012

2-2-2 Reasons for any changes of the schedule, and their effects on the project.

1. EXTENSION OF TERM

- Group "A": Different conditions of land and electromechanical part,

Cessation of regional unemployment

- Group "B": the extension of goals for more meters.

Cessation of regional unemployment

- *Group* "C":

Easement issues in phase 1

Different conditions in step 3

Stroke change collector AD 1

Change of diameter in the transmitter

(P/R and PCIV

(Unit: Million)

2-3 Project Cost

2-3-1

Table 2-3-la: Comparison of Original and Actual Cost BY ITEM

Breakdown of Cost	Original								
	Foreign Cu	Foreign Currency Portion Local Currency Portion				Total			
	Total	JICA	Peru	Total	JICA I	Peru Portion	Total	JICA	Peru
		Portion	Portion		Portion			Portion	Portion
Item	n	nillionJPY		r	nillion SOL		1	millionJPY	
Procurement/Installation	154	78	76	312	140	172	11,133	4,995	6,138
1 - South Zone	0	0	0	84	42	42	2,937	1,471	1,466
Water Supply Portion	0	0	0	32	16	16	1,161	581	580
Sewerage Portion	0	0	0	52	26	26	1,776	890	886
2- Central Zone	0	0	0	78	39	39	2,761	1383	1,378
Water Supply Portion	0	0	0	32	16	16	1,128	565	563
Sewerage Portion	0	0	0	46	23	23	1,633	818	815
3- North Zone	0	0	0	58	29	29	2,042	1,023	1,019
Water Supply Portion	0	0	0	24	12	12	846	424	422
Sewerage Portion	0	0	0	34	17	17	1,196	599	597
Total of Civil Work	0	0	0	220	110	110	7,740	3,877	3,863
Consulting Services	70	70	0	23	23	0	876	876	0
Price Escalation	4	4	0	0	0	0	4	4	0
Physical Contingencies	4	4	0	12	7	5	431	238	193
Land Aquistion	0	0	0	0	0	0	14	0	14
Administration	0	0	0	8	0	8	272	0	272
Tax and Duties	0	0	0	49	0	49	1,720	0	1,720
Interest during Construction	56	0	56	0	0	0	56	0	56
Commitment Charge	20	0	20	0	0	0	20	0	20
Total	154	78	76	312	140	172	11,133	4,995	6,138

(Note) Exchange Rate: (1) USD 1=TPY111, (2) USD1=Sol 3.16, (3) Soll=IPY35.2

Base Year for Cost Estimation: October 8, 2008

(Unit: Million)

Breakdown of Cost	Original								
	Foreign Cu	Foreign Currency Portion Local Currency Portion				Total			
	Total	JICA	Peru	Total	JICA	Peru Portion	Total	JICA	Peru
		Portion	Portion		Portion			Portion	Portion
Item	m	nillionJPY		n	nillion SOL		r	nillionJPY	
Procurement/Installation	154	78	76	392	150	239	11,804	4,628	7,175
1- South Zone	0	0	0	116	47	67	3,307	1,379	1,928
Water Supply Portion	0	0	0	52	19	32	1,481	567	915
Sewerage Portion	0	0	0	64	28	35	1,825	812	1013
2- Central Zone	0	0	0	99	41	57	2,846	1,199	1,646
Water Supply Portion	0	0	0	37	14	23	1,072	410	662
Sewerage Portion	0	0	0	62	27	34	1,774	789	985
3- North Zone	0	0	0	78	32	46	2,258	932	1,326
Water Supply Portion	0	0	0	40	15	25	1,160	444	716
Sewerage Portion	0	0	0	38	17	21	1,098	488	609
Total of Civil Work	0	0	0	293	120	170	8,411	3,510	4,900
Consulting Services	70	70	0	23	23	0	876	876	0
Price Escalation	4	4	0	0	0	0	4	4	0
Physical Contingencies	4	4	0	12	7	5	431	238	193
Land Aquistion	0	0	0	0	0	0	14	0	14
Administration	0	0	0	8	0	8	272	0	272
Tax and Duties	0	0	0	49	0	49	1,720	0	1,720
Interest during Construction	56	0	56	0	0	0	56	0	56
Commitment Charge	20	0	20	0	0	0	20	0	20
Total	154	78	76	385	150	232	11,804	4,628	7,175

(Note) Exchange Rate: (1) USD 1=TPY111, (2) USD1=Sol 3.16, (3) Soll=IPY35.2

Table 2-3-lb: Comparison of Original and Actual Cost BY YEAR

*Fiscal Year starring in <u>January</u> and ending in <u>December</u> (Unit: Million)

Breakdown of Cost		Original			Actual	
	JICA Portion	Others	Total	JICA Portion	Others	Total
Year	(YEN)	(YEN)	(YEN)	()	()	()
2009	205	64	269	279.3	34.02	313.32
2010	2,088	2,619	4,707	2,203	1,820	4,022.58
2011	2,702	3,427	6,129	2,147	5,322	7,468
2012	0	28	28	0	0	0
Total	4,995	6,138	11,133	4,628	7,175	11,804

Note: Exchange Rate used: (1) USD 1=TPY111, (2) USD1=Sol 3.16, (3) Soil=JPY35.2

You can use any currencies in this chart, i.e. you may use your local currency as well as Yen for each figure. If there were the portion of the financial resources such as of World Bank, IDB and so forth, other than your own budget, please fill in another column between "JICA Portion" and "Others" and fill in the figures of them


2-3-2 Reason(s) for the wide gap between the original and actual, if there have been any, the remedies you have taken, and their results.

(P/R, PCRJ

2-4 Organizations for Implementation

2-4-1 Executing Agency:

Organization's role, financial position, capacity, cost recovery etc, Organization Chart including the unit in charge of the implementation and number of employees.

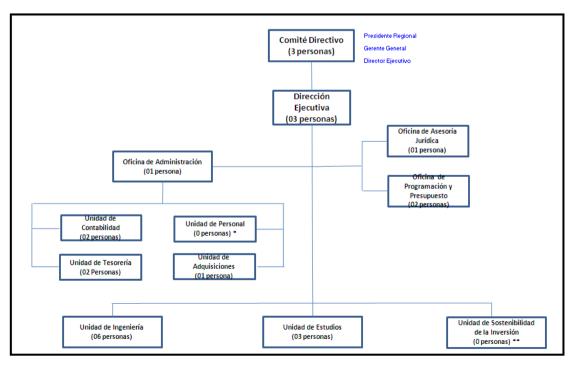

- (*)The unit this of personnel assuming these functions the administrator
- (**)The Division of sustainability of the investment is not activated.

Original: (P/M)

(1) Regional Government of Cajamarca (RGC)

[Position] Executing Agency

[Role] Authorized agency to submit any official request for JICA, in charge of all function necessary for the execution of the Project, except those in charge of EPS SEDACAJ and EPS Maranon.

[Total personal] 300(excluding supporting staff)

[Responsible unit] Proyectos Especiales

The Project will be implemented through U.E 005 Programas Regional (PROREGION) to be created in GRC, established under Gerencia General Regional of GRC and GRC will be responsible for the supervision of die implementation of the project and financing and repayment of the project.

(2) EPS SEDACAJ and EPS Marañon

	ESP SEDACAJ	EPS MARANON
Position	Implementing Agency	Implementing Agency
Total Personal	145	60
	(excluding supporting staff)	(excluding supporting staff)
Responsible	Gerencia Operaciones	Gerencia Operaciones
Unit		
Provinces	San Marcos, Cajabamba, Celendin,	Jaen
	Hualgayoc, San Pablo, Bambamarca,	
	Chota, Cutervo, Contumaza, San	
	Miguel	
Responsibilities	Responsible for operation and	Responsible for operation and
	maintenance after the completion	maintenance after the completion
	of the Project and subscription of civil	of the Project and subscription of civil
	work contracts.	work contracts.

(3) Ministerio de Vivienda, Construcción y Saneamiento (MVCS)

[Position] Monitoring Agency

[Role] In charge of the monitoring of the activities of RGC and SEDACAJ and MARANON

[Responsible unit] Dirección Nacional de Saneamiento (DNS)

MVCS will monitor the activities of the Executing and Implementing Agencies and, if necessary, provides assistance. It also provides a part of resources necessary for counterpart fund of the Project.

Actual, if changed: (P/R and PCR)

2-4-2 Contractor(s)/ Supplier(s), and Consultant(s) and Their Performance:

2-4-2-1 Procurement and Consultant

Contract Package	Selection Method	
	Original: (P/M)	Actual: (P/R and PCR)
1. Group A (south)	ICB with PQ*	
2. Group B (central)	ICB with PQ*	Keep it
3. Group C (north)	ICB with PQ*	
Consultant (Engineering, EIA preparation, support for bidding process, supervision and project management and capacity building)	Short-list	Keep it

^{*} $p_{\rm re}$ Qualification will be implemented with the Bidding process.

2-4-2-2 Performance

(P/R and PCR)

Information on the Contractor(s)/ Supplier(s):

GROUPS OF			(%) PH	IYSICAL ADVANCE	
WORK	CITY	WATER SUPPLY	SEWERAGE	TOTAL TRIMESTRE	AVANCE GENERAL
	CONTUMAZA	14.22	10.8	12.26	94.08
	CELENDÍN	3.78	7.64	5.85	66.45
GROUP`"A"	SAN MIGUEL	0	0	0	65.64
GROUP A	SAN MARCOS	0	0	0	74.04
	CAJABAMBA	6.08	11.94	9.9	74.63
	SAN PABLO	0	0	0	79.55
	СНОТА	5.46	4.01	4.64	32.5
GROUP "B"	HUALGAYOC	3.05	8.79	6.06	25.46
GROUP B	BAMBAMARCA	11.52	2.25	6.1	27.28
	CUTERVO	10.24	3	4.67	36.13
GROUP "C"	JAÉN	2.63	3.28	2.95	46.39

Note: Valuation of work N $^{\circ}$ 21 (March 30, 2012)

Evaluation:

The Group "B":

In The City Of Chota

 Failure to pay the workers generates paralyzation of the work and conflict with committee work

In The City Of Hualgayoc

• abandoned trenches slope sliding speed to homes, prompting protests from the residents affected

In The City Of Cutervo

- owners through which the issuer does not give the pass
- Failure to pay the workers generates paralyzation of the work and conflict with committee work

The Group "C":

In The City Of Jaen

- project blame the resurgence of dengue in the city
- easement landowners seeking renegotiation of amounts paid
- •residents of the hamlet of low pingobamba refuse to the construction of the PTAR

Information on the Consultant(s):

Evaluation:

2-5 Precautions (Measures To Be Adopted/Points Which Require Special Attention)

- Risks and issues, if any, which may affect the project implementation and planned countermeasures to be adapted, in terms of physical, environmental or social aspects.(e.g., land acquisition, resettlement, HIV awareness and prevention program, gender consideration and EIA clearance).
- Environmental Checklist or report of monitoring indicator (if applicable).

Original issues and Countermeasure(s)	Actual issues and Countermeasure(s)
(P/M)	(P/R and PCR)
(1) WWTPs in 4 sub-projects Following 4 WWTPs will be constructed by own resources of GOP. The progress of such WWTPs shall be informed in P/R. - San Miguel (MVCS) - Contumaza (MVCS)	a) With regard to the Plant of Treatment of San Miguel, the construction has been reached by the EPS SEDACAJ SA, and nowadays the observations are getting up. b) The Plant of Contumaza's Treatment, nowadays he is in bidding and still the works do not begin. c) In the Plant of Treatment of San Pablo, works of conditioning are beginning.

- San Pablo (GRC) - San Marcos (GRC)	d) In the plant of Treatment of San Marcos, the works already have been concluded.
(2) Water Right In Hualgayoc, San Miguel and San Marcos, it is necessary to obtain right for more use of water to Autoridad Nacional del Agua del Ministerio de Agricultura, before the consulting services begins.	Already one possesses the Law of the Water.

2-6 Photographs of Output of the project (P/R and PCR)-. Attachment

3: Benefit Derived from the Project (Effectiveness)

3-1 Operational and physical condition of each facility developed/supplied by the project.

Facilities	Description of condition	Problems, its Background and Remedial
		Action Plan
(P/R and PCR)	(P/R and PCR)	(P/R and PCR)

3-2 Precautions (Measures To Be Adopted/Points Which Require Special Attention)

- Risks and issues, if any, which may affect the project outcome and planned countermeasures to be adapted, in terms of physical, environmental or social aspects.
- Environmental Checklist or report of monitoring indicator (if applicable)

Original issues and Countermeasure(s)	Actual issues and Countermeasure(s)
(P/M)	(P/R and PCR)
(1) Land Acquisition	The land has been acquired by local governments
9 cities except Contumaza and San Pablo need Land	The land has been acquired by local governments
Acquisition and yet to be acquired. It is expected to	
end at least before the consulting services begins.	
(2) EIA clearance	
EIA will be prepared by the consulting services. EIA	Corrently has the EIA
approval will be obtained before the civil work begins.	

3-3 Environmental and Social Impacts

- Major environmental and social impacts have occurred during project implementation (e.g. involuntary resettlement, poverty reduction, natural environment)

Issue(s)	Action or countermeasure(s) taken and remaining problem(s)
(PCR)	(PCR)

(1) Involuntary Resettlement The Project does not expect any involuntary resettlements.	
(2) Poverty Reduction Poverty rate in Cajamarca (74%) is higher than National rate (51%). In addition, free domestic connections are included in the project to assist the poor, who otherwise will not have house connections.	

3-4 Qualitative and Quantitative Data of Monitoring Indicators

- Operation and Effect Indicator, EIRR and/or FIRR
- Supporting data for computing EIRR and/or FIRR.

EIRR and FIRR for the Project

Water Supply a	Vater Supply and Sewerage		
EIRR	Original	Actual	
	14.74% (Water Supply)		
	-Cost: Project cost (excluding escalation, tax)		
	and O&M cost.		
	-Benefit: (a) Saving time and cost for	Keep it	
	supplying water, (b) benefits by continuing water	1.00p 11	
	services		
	-Project life: 20 years		
	11.90% (Sewerage)		
	-Cost: Project cost (excluding escalation, tax		
	and duties) and O&M cost.		
	-Benefit: (a) Improved health conditions		
	(saving money for health cost), (b) increased		
	number of tourists		
	-Project life: 20 years		
FIRR	6.47% (Water Supply + Sewerage)		
	-Cost: Project cost (excluding escalation, tax		
	and duties) and O&M cost.		
	-Benefit: (a) revenue accrued from increased	Keep it	
	service recipients		
	-Finance: JICA financing		
	-Project life: 20 years		

EIRR and FIRR: Indicators JICA.

Indicators for Water supply and Sewerage components

Group A

Cajabamba

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population served	8,631		13,255
2 Water Supply Hours/day	16		24 hours
3 Percentage of Population Served (%)	59.4 %		90.0%

L/A NO. PE-P35 PSR prepared on June 27, 2012

4 Number of House Connections	2,105	3,233
Indicators for Sewerage		
1 Total Population Served	12,300	13,255
2 Amount of Wastewater Treated (m / day)	0	1,122
3 Percentage of Population Served (%)	84.7 %	90.0%
4 Number of House Connections	3,000	3,233
5 Effluent BOD ² (mg/1)	-	78

2 Measuremet for 5 Effluent BOD is taken from the exit of WWT, before being discharged into rivers. Therefore, the rate of effluent BOD is not equivalent to the Peruvian standard.

Celendin

Celenani			
Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population served	12,564		15,322
2 Water Supply Hours/day	24 hours (rainy season) 16 hours (dry season)		24 hours
3 Percentage of Population Served (%)	75.1%		90.0%
4 Number of House Connections	3,255		3,969
Indicators for Sewerage			
1 Total Population Served	12,564		15,322
2 Amount of Wastewater Treated (m / day)	0		1,303
3 Percentage of Population Served (%)	75.1%		90.0%
4 Number of House Connections	3,255		3,969
5 Effluent BOD (mg/1)	-		67

Contumaza

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population served	2,804		2,996
2 Water Supply Hours/day	24		24 hours
3 Percentage of Population Served (%)	87.1 %		93.0%
4 Number of House Connections	827		884
Indicators for Sewerage			
1 Total Population Served	2,698		2,996
2 Amount of Wastewater Treated (m/day)	0		210
3 Percentage of Population Served (%)	83.8 %		93.0%
4 Number of House Connections	796		884

SAN MIGUEL

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yr 1)
1 Total Population Served	2,964		3,494
2 Water Supply Hours/day	20 hours		24 hours
3 Percentage of Population Served (%)	81.5%		93.0%
4 Number of House Connections	912		1,075
Indicators for Sewerage			
1 Total Population Served	2,584		3,494
2 Amount of Wastewater Treated (nf/dav)	0		252
3 Percentage of Population Served (%)	71.10%		93.0%
4 Number of House Connections	795		1,075
5 Effluent BOD (mg/1)	-		-

San Pablo

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yr1)
1 Total Population treated	2,346		2,775
2 Water Supply Hours/day	4 hours (dry season) 14 hours (rainy season)		24 hours
3 Percentage of Population Served (%)	79.6%		93.0%
4 N umber of House Connections	841		995
Indicators for Sewerage			
1 Total Population Served	2,232		2,775
2 Amount of Wastewater Treated (rn/day)	0		265
3 Percentage of Population Served (%)	75.8%		93.0%
4 Number of House Connections	800		995
5 Effluent BOD (mg/I)	-		-

San Marcos

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yr1)
1 Total Population treated	5,919		7,081
2 Water Supply Hours/day	22 hours (rainy season) 6 hours (dry season)		24 hours
3 Percentage of Population Served (%)	77.7%		90.0%
4 Number of House Connections	1,506		1,802
Indicators for Sewerage			
1 Total Population Served	4,464		7,081
2 Amount of Wastewater Treated (m /day)	0		709
3 Percentage of Population Served (%)	58.6%		90.0%
4 Number of House Connections	1,136		1,802
5 Effluent BOD (mg/1)	-		-

Group B

Bambamarca

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population Served	8,104		15,541
2 Water Supply Hours/da}'	Lower area 24hours Upper area 1 hour		24 hours
3 Percentage of Population Served (%)	45.6%		85.0%
4 Number of House Connections	2,412		4,625
Indicators for Sewerage			
1 Total Population Served	8,242		15,541
2 Amount of Wastewater Treated (m/day)	0		1,444
3 Percentage of Population Served (%)	46.4%		85.0%
4 Number of House Connections	2,453		4,625
5 Effluent BOD (mg/1)	-		62

Chota

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population Served	12,491		16,927
2 Water Supply Hours/day	3 hours		24 hours
3 Percentage of Population Served (%)	67.7%		90.0%
4 Number of House Connections	4,220		5,719
Indicators for Sewerage			
1 Total Population Served	10,360		16,927
2 Amount of Wastewater Treated (m/day)	0		1,531
3 Percentage of Population Served (%)	56.1 %		90.0%
4 Number of House Connections (thousand)	3,500		5,719
5 Effluent BOD (mg/1)	-		60

Cutervo

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 Total Population Served	9,992		13,402
2 Water Supply Hours/day	9 hours		24 hours
3 Percentage of Population Served (%)	65.1%		85.0%
4 Number of House Connections	2,791		3,744
Indicators for Sewerage			
1 Total Population Served	11,456		13,402
2 Amount of Wastewater Treated (m'/day)	0		1,102
3 Percentage of Population Served (%)	74.7%		85.0%
4 Number of House Connections	3,200		3,744
5 Effluent BOD (mg/1)	-		80

Hualgayoc

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yrl)
1 (Total Population Served	1,256		1,354
2 Water Supply Hours/day	16hours (rainy season) 6 hours		24 hours
	(dry season)		
3 Percentage of Population Served (%)	87.6%		94.5%
4 Number of House Connections	405		437
Indicators for Sewerage			
1 Total Population Served	1,240		1,354
2 Amount of Wastewater Treated (ni/day)	0		134
3 Percentage of Population Served (%)	86.5%		94.5%
4 Number of House Connections	400		437
5 Effluent BOD (mg/1)	-		15

GRUPO C

Jaen

Indicators for water supply	Original (Yr 2007)	Present (Yr)	Target (Yr1)
1 Total Population Served	47,736		59,447
2 Amount of Treated Water (L/ day)	14,515,200		21′697,314
3 Water Supply Hours / day	14 hours		24 hours
4 Percentage of Population Served (%)	73.7%		89.0%
Number of House Connections	12,529		15,603*
Indicators for Sewerage			
1 Total Population Served	45,396		59,447
2 Amount of Wastewater Treated (m³/day)	7,599		9,806
3 Percentage of Population Served (%)	63.4%		89.0%
4 Number of House Connections	10,499		15,603*
5 Effluent BOD (mg/1)	342		32

(*) The project of code SNIP 82443 at the expense of the municipality of Jaen, it has the same area of intervention (Huito's San Jose) that partly there forms the Project "Improvement and Extension of the system of drinkable water, sewer and treatment of waste water of the city of Jaen "with code SNIP 61434 at the expense of the Executing Unit - PROREGIÓN; nevertheless the latter already has been executed by the contractor - RECEIVES FACILITIES AND SERVICES S.A.

3.6 Monitoring Plan for the indicators

Monitoring methods, section(s)/department(s) in charge of monitoring, frequency, the term and so forth.

Original: (P/M and PCR)

EPS SEDACAJ and EPS Marañon shall conduct monitoring of the above mentioned indicators (other than health indicator) every three months in accordance with SUNASS regulation and Ministry of Health and will conduct monitoring of the health indicator once a year.

Actual: (P/R and PCR)

3.7 Achievement of the Project Objective

(PCR)

4: Operation and Maintenance (O&M) (Sustainability)

4-1 O&M and Management

- Organization chart of O&M - Operational and maintenance system (structure and the number /qualification and skill of staff or other conditions necessary to maintain the outputs and benefits of the project soundly, such as manuals, facilities and equipment for maintenance, and spare part stocks etc)

Original: (P/M)

O&M Scheme:

1. Once the civil work components are completed, EPS SEDACAJ and EPS Marahon will be responsible for O&M. 8 cities currently served by the municipalities will be incorporated to the service area of SEDACAJ, as shown below.

City	Entity	
Cajabamba	EPS SEDACAJ	
Celendin	EPS SEDACAJ	
Contumaza	EPS SEDACAJ	
San Pablo	EPS SEDACAJ	
San Miguel	EPS SEDACAJ	
San Marcos	EPS SEDACAJ	
Bambamarca	EPS SEDACAJ	
Chota	EPS SEDACAJ	
Cutervo	EPS SEDACAJ	
Hualgayoc	EPS SEDACAJ	
Jaen	EPS Marañon	

(8 cities to be incorporated to EPS SEDACAJ are identified by color)

2. Since EPS SEDACAJ and EPS Marañon has limited experience with Water and Waste Water treatment plants, O&M training will be provided by consulting services.

3. O&M Cost

O&M Cost will be recovered by water service fee.

4-2 O&M Cost and Budget

- The actual annual O&M cost for the duration of the project up to today, as well as the annual O&M budget.

(PCR)

5: Evaluation

5-1 JICA and Borrower/Executing Agency Performance

Please evaluate the performance of the two bodies.

JICA: (PCR)

Borrower/Executing Agency:

(PGR)

5-2 Overall evaluation

Please describe your evaluation on the overall outcome of the project.

(PCR)

5-3 Lessons Learnt and Recommendations

Please raise any lessons learned from the project experience, which might be valuable for the future JICA assistance or similar type of projects, as well as any recommendations, which might be beneficial for better realization of the project effect, impact and assurance of sustainability.

(PCR)

Annex II

Forecast Disbursement Schedule

CY	2009					20_
Item	Jan-Mar	Api-Jun	Jul-Sep	Oct-Dec	Total	
Total						

Α n n

е
